

COMMISSIONINGREQUEST FORM

Please be aware the boiler must be commissioned within 3 months of the installation date to qualify for the full warranty.

SITE DETAILS		
Site contact name Mark Cleverley	Site name Sanctuary Housing Association Head Office	
Site contact number 1 01782710147	Site contact number 2 07469245273	
Site address Sanctuary Housing Association Chamber Court Castle Street Worcester	Site Postcode WR1 3zq	

	BOILER 1	
Boiler model		
Heat 2		

Output
45kW

Full serial number
AFL22082100000348


Date code
25/01/21

Installation date
22-Apr-21

Purchase date
26-Mar-21

Merchant purchased from
Heating Control & Spares HCS

Branch
Chester

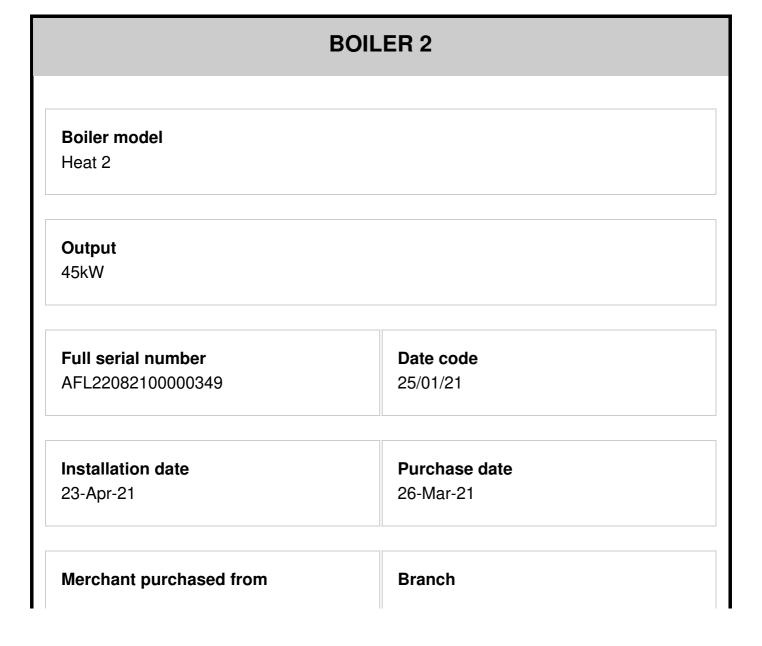

BOILER 3

Boiler model

Heat 2

Output

45kW

Full serial number

AFL22082100000148

Date code

25/01/21

Installation date

23-Apr-21

Purchase date

26-Mar-21

Merchant purchased from

Heating Controls & Spares HCS

Branch

Chester

BOILER 4

Boiler model

Heat 2

Output

45kW

Full serial number
AFL22082100000350

Installation date
23-Apr-21

Merchant purchased from
Heating Controls & Spares HCS

Installed options
Safety interlock kit

BOILER 5		
Boiler model		
Heat 2		
Output		
45kW		
Full serial number	Date code	
AFL22082100000351	25/01/21	
Installation date	Purchase date	
	26-Mar-21	

Merchant purchased from

Heating Controls & Spares HCS

Branch

Chester

BECAUSE YOU SELECTED MORE THAN ONE HEAT 2, PLEASE COMPLETE THE BELOW FIELDS.

Varican Gateway Master kit fitted?

No

Varican Gateway Slave kit(s) fitted?

No

Extension Module kit fitted?

No

Has a Frame and Header kit been used in the installation?

No

Which kit was used?

Flow Sensor Immersion Pocket kit fitted?

No

Has a Keston Low Loss Header been used?

No

Flow Sensor Strap On kit fitted?

No

0-10V Pump kit fitted?

Yes

INSTALL	.ER D	ETAILS)
---------	-------	--------	---

Contact name

Mark Cleverley

Contact number

01782710147

Company name

Ford Mainwaring Limited

Email address

mark@fordmainwaring.co.uk

Company Gas Safe Registration

10326

Company address

Ford Mainwaring Ltd, Unit 702 Lowfield Drive, Centre 500

Company Postcode

ST5 0UU

APPOINTMENT DETAILS

Requested visit date

06/05/2021

Is a Site Induction necessary?

Yes

Time Needed

Less than 20 minutes

Do our engineers require CSCS cards?

No

Are Risk Assessment / Method Statements required?

No

Please note the system must be cold and have sufficient heat load so all boilers can be fired full rate

REPORTS

Please provide at least 2 email addresses for the report and warranty certificate (where applicable) upon completion of a successful commissioning

Email address 1

mark@fordmainwaring.co.uk

Email address 2

info@fordmainwaring.co.uk

Are you happy to receive information alongside this report detailing our service & care packages?

Yes

INSTALLATION DETAILS

All of the below must be completed for us to carry out the commissioning.

Please give details of any special instructions in the box provided at the bottom.

Should we be unable to carry out the work, we reserve the right to make a charge for the full cost of the visit.

Any calls cancelled without 24 hours notice may be charged at the full commissioning cost.

Is adequate purpose built ventilation	
installed?	

Yes

What percentage has this been calculated 100% at?

Is ventilation mechanical or natural?

Natural

Does the flue comply with BS:6644, BS:5440, IGE UP/10 & CE Approved?

Yes

How is the flue installed?

Horizontally

Has the electrical supply been connected Yes

with option to isolate?

Has water been connected, boiler filled

and air removed?

10.1

Has the gas been connected and purged? Yes

Have external controls been commissioned & operational?

Yes

Yes

Is a permanent light available in the boiler Yes

room?

Is the boiler showing any faults?	No
Is the boiler showing any faults?	No
Is the boiler fully accessible?	Yes
Is adequate onsite parking available?	Yes
Has the system been cleansed before installation?	Yes
Has the system been dosed since installation?	Yes

Additional site information

Boilers are ready to be commission and are connected to the existing BMS 0-10v control

COST BREAKDOWN		
Commissioning costs		
Heat 2	£125.00	
Heat 2	£60.00	
Total Commissioning Costs	£365.00	
Site induction costs		
20 minute induction	£0.00	
Total Induction Costs	£0.00	
Total Costs	£365.00	

CONFIRMATION BY

Full name	
Mark Cleve	rley

Email address

mark@fordmainwaring.co.uk

I confirm that I have completed this form as accurately as possible and that any incorrect information provided may lead to delays and/or return visits, which may be chargeable. I am aware that my requested commissioning date may not be available.

Confirmation of your visit date will be supplied within 2 working days

I confirm I have read the Terms & Conditions of use for keston.co.uk. As a data controller, Keston Boilers Ltd take the protection of your personal data seriously. To view our Privacy Policy, please click here.
